

Activity ID	Activity Name	Original Duration	Actual Duration	Duration % Complete	Start	Finish	2025											
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
GMP-1350	BP23B HVAC/Controls	7	0	0%	05-Nov-24	14-Nov-24	■ BP23B HVAC/Controls											
GMP-1360	BP26B Electrical	7	0	0%	05-Nov-24	14-Nov-24	■ BP26B Electrical											
GMP-1370	BP27A Low Voltage/Security	7	0	0%	05-Nov-24	14-Nov-24	■ BP27A Low Voltage/Security											
GMP-1120	BP01B Final Clean Contract Award	7	0	0%	12-Nov-24	20-Nov-24	■ BP01B Final Clean Contract Award											
GMP-1170	BP03A Concrete Foundations/Slabs Contract Award	7	0	0%	12-Nov-24	20-Nov-24	■ BP03A Concrete Foundations/Slabs Contract Award											
GMP-1190	BP04B Masonry Contract Award	7	0	0%	12-Nov-24	20-Nov-24	■ BP04B Masonry Contract Award											
GMP-1200	BP05A Metal Fab & Misc. Metals Contract Award	7	0	0%	12-Nov-24	20-Nov-24	■ BP05A Metal Fab & Misc. Metals Contract Award											
GMP-1220	BP08A Glazing/Storefront Contract Award	7	0	0%	12-Nov-24	20-Nov-24	■ BP08A Glazing/Storefront Contract Award											
GMP-1230	BP09A Doors/Hardware	7	0	0%	12-Nov-24	20-Nov-24	■ BP09A Doors/Hardware											
GMP-1240	BP09B Studs/Drywall/Ceilings	7	0	0%	12-Nov-24	20-Nov-24	■ BP09B Studs/Drywall/Ceilings											
GMP-1250	BP09C Painting/Walkcoverings	7	0	0%	12-Nov-24	20-Nov-24	■ BP09C Painting/Walkcoverings											
GMP-1260	BP09D Tile	7	0	0%	12-Nov-24	20-Nov-24	■ BP09D Tile											
GMP-1270	BP09E Wood Flooring	7	0	0%	12-Nov-24	20-Nov-24	■ BP09E Wood Flooring											
GMP-1280	BP09F Resilient Flooring	7	0	0%	12-Nov-24	20-Nov-24	■ BP09F Resilient Flooring											
GMP-1290	BP10A Specialties	7	0	0%	12-Nov-24	20-Nov-24	■ BP10A Specialties											
GMP-1310	BP12A Millwork/Casework	7	0	0%	12-Nov-24	20-Nov-24	■ BP12A Millwork/Casework											
GMP-1320	BP12B Loose Furnishings	7	0	0%	12-Nov-24	20-Nov-24	■ BP12B Loose Furnishings											
GMP-1380	BP31A Site Utilities/Hardscapes	7	0	0%	12-Nov-24	20-Nov-24	■ BP31A Site Utilities/Hardscapes											
GMP-1390	BP32A Landscaping	7	0	0%	12-Nov-24	20-Nov-24	■ BP32A Landscaping											
Construction Documents		50	110	100%	28-May-24 A	31-Oct-24												
CD-1010	Publish Documents (Long Lead Procurement & Demo/Abatement)	5	5	100%	28-May-24 A	03-Jun-24 A	■ Demo/Abatement											
CD-1000	Publish GMP 75% Construction Documents	28	28	100%	24-Jun-24 A	01-Aug-24 A	■ Construction Documents											
CD-1020	Publish 100% CD Documents	22	63	100%	02-Aug-24 A	31-Oct-24	■ Publish 100% CD Documents											
Board Meetings		97	97	100%	21-May-24 A	08-Oct-24 A												
BM-1000	May Board Meeting	0	0	100%		21-May-24 A	■ Board Meeting											
BM-1010	June Board Meeting	0	0	100%		10-Jun-24 A	■ Board Meeting											
BM-1020	July Board Meeting	0	0	100%		09-Jul-24 A	■ Board Meeting											
BM-1030	August Board Meeting	0	0	100%		06-Aug-24 A	■ Board Meeting											
BM-1040	September Board Meeting	0	0	100%		11-Sep-24 A	■ Board Meeting											
BM-1050	October Board Meeting	0	0	100%		08-Oct-24 A	■ Board Meeting											
AHJ		63	43	68.25%	30-Aug-24 A	02-Dec-24												
AHJ-1010	Demo Permit	1	43	100%	30-Aug-24 A	30-Oct-24 A	■ Demo Permit											
AHJ-1020	Building Permit	20	0	0%	31-Oct-24	02-Dec-24	■ Building Permit											
Procurement		211	8	8.06%	14-Oct-24 A	07-Aug-25												
Submittals		46	8	36.96%	14-Oct-24 A	13-Dec-24												
Early Release Package Submittals		27	8	62.96%	14-Oct-24 A	14-Nov-24												
SUB-1000	BP02A Mass Demolition - Submittals	5	8	100%	14-Oct-24 A	23-Oct-24 A	■ BP02A Mass Demolition - Submittals											

Start Date: 19-Dec-23
 Finish Date: 31-Oct-25
 Data Date: 31-Oct-24
 Run Date: 04-Nov-24 16:21
 Page 2 of 8
 SL-1

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Summary Milestones
- ◆ Critical Milestones
- ◆ Milestone

Shaker Ludlow

Activity ID	Activity Name	Original Duration	Actual Duration	Duration % Complete	Start	Finish	2025											
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
SUB-1040	BP14A Elevator - Submittals	10	0	0%	31-Oct-24	14-Nov-24	■ BP14A Elevator - Submittals											
SUB-1050	BP23A Mechanical Equipment Early Procurement - Submittals	10	0	0%	31-Oct-24	14-Nov-24	■ BP23A Mechanical Equipment Early Procurement - Submittals											
SUB-1060	BP26A Electrical Equipment Early Procurement - Submittals	10	0	0%	31-Oct-24	14-Nov-24	■ BP26A Electrical Equipment Early Procurement - Submittals											
Construction Package Submittals		22	0	0%	12-Nov-24	13-Dec-24												
SUB-1010	BP04A Masonry Restoration (Design Assist) - Submittal	15	0	0%	12-Nov-24	04-Dec-24	■ BP04A Masonry Restoration (Design Assist) - Submittal											
SUB-1130	BP07A Roofing (Design Assist) - Submittal	15	0	0%	12-Nov-24	04-Dec-24	■ BP07A Roofing (Design Assist) - Submittal											
SUB-1250	BP21A Fire Protection - Submittal	15	0	0%	15-Nov-24	09-Dec-24	■ BP21A Fire Protection - Submittal											
SUB-1260	BP22A Plumbing - Submittal	15	0	0%	15-Nov-24	09-Dec-24	■ BP22A Plumbing - Submittal											
SUB-1270	BP23B HVAC/Controls - Submittal	15	0	0%	15-Nov-24	09-Dec-24	■ BP23B HVAC/Controls - Submittal											
SUB-1280	BP26B Electrical - Submittal	15	0	0%	15-Nov-24	09-Dec-24	■ BP26B Electrical - Submittal											
SUB-1290	BP27A Low Voltage/Security - Submittal	15	0	0%	15-Nov-24	09-Dec-24	■ BP27A Low Voltage/Security - Submittal											
SUB-1100	BP03A Concrete Foundations/Slabs - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP03A Concrete Foundations/Slabs - Submittal											
SUB-1110	BP04B Masonry - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP04B Masonry - Submittal											
SUB-1120	BP05A Metal Fab & Misc. Metals - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP05A Metal Fab & Misc. Metals - Submittal											
SUB-1140	BP08A Glazing/Storefront - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP08A Glazing/Storefront - Submittal											
SUB-1150	BP09A Doors/Hardware - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP09A Doors/Hardware - Submittal											
SUB-1160	BP09B Studs/Drywall/Ceilings - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP09B Studs/Drywall/Ceilings - Submittal											
SUB-1170	BP09C Painting/Walkcoverings - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP09C Painting/Walkcoverings - Submittal											
SUB-1180	BP09D Tile - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP09D Tile - Submittal											
SUB-1190	BP09E Wood Flooring - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP09E Wood Flooring - Submittal											
SUB-1200	BP09F Resilient Flooring - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP09F Resilient Flooring - Submittal											
SUB-1210	BP10A Specialties - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP10A Specialties - Submittal											
SUB-1230	BP12A Millwork/Casework - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP12A Millwork/Casework - Submittal											
SUB-1240	BP12B Loose Furnishings - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP12B Loose Furnishings - Submittal											
SUB-1300	BP31A Site Utilities/Hardscapes - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP31A Site Utilities/Hardscapes - Submittal											
SUB-1310	BP32A Landscaping - Submittal	15	0	0%	21-Nov-24	13-Dec-24	■ BP32A Landscaping - Submittal											
Approvals		55	4	40%	18-Oct-24 A	06-Jan-25												
Early Release Package Approvals		36	4	61.11%	18-Oct-24 A	06-Dec-24												
SUB-1020	BP02A Mass Demolition - Approval	14	4	100%	18-Oct-24 A	23-Oct-24 A	■ BP02A Mass Demolition - Approval											
SUB-1070	BP14A Elevator - Approval	14	0	0%	15-Nov-24	06-Dec-24	■ BP14A Elevator - Approval											
SUB-1080	BP23A Mechanical Equipment Early Procurement - Approval	14	0	0%	15-Nov-24	06-Dec-24	■ BP23A Mechanical Equipment Early Procurement - Approval											
SUB-1090	BP26A Electrical Equipment Early Procurement - Approval	14	0	0%	15-Nov-24	06-Dec-24	■ BP26A Electrical Equipment Early Procurement - Approval											
Construction Package Approvals		21	0	0%	05-Dec-24	06-Jan-25												
SUB-1350	BP04A Masonry Restoration (Design Assist) - Approval	14	0	0%	05-Dec-24	24-Dec-24	■ BP04A Masonry Restoration (Design Assist) - Approval											
SUB-1380	BP07A Roofing (Design Assist) - Approval	14	0	0%	05-Dec-24	24-Dec-24	■ BP07A Roofing (Design Assist) - Approval											
SUB-1500	BP21A Fire Protection - Approval	10	0	0%	10-Dec-24	23-Dec-24	■ BP21A Fire Protection - Approval											
SUB-1510	BP22A Plumbing - Approval	14	0	0%	10-Dec-24	30-Dec-24	■ BP22A Plumbing - Approval											

Start Date: 19-Dec-23
 Finish Date: 31-Oct-25
 Data Date: 31-Oct-24
 Run Date: 04-Nov-24 16:21
 Page 3 of 8
 SL-1

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Summary Milestones
- Critical Milestones
- Milestone

Shaker Ludlow


Activity ID	Activity Name	Original Duration	Actual Duration	Duration % Complete	Start	Finish	2025															
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec		
IRI-1340	L2 - Interior Studs	15	0	0%	09-Jan-25	29-Jan-25			█													
IRI-1350	L2 - Fire Protection	12	0	0%	09-Jan-25	24-Jan-25			█													
IRI-1430	L2 - Door Frames / Storefronts	15	0	0%	09-Jan-25	29-Jan-25			█													
IRI-1380	L2 - Electrical	15	0	0%	16-Jan-25	05-Feb-25			█													
IRI-1390	L2 - Technology / AV	15	0	0%	16-Jan-25	05-Feb-25			█													
IRI-1410	L2 - Fire Alarm	10	0	0%	16-Jan-25	29-Jan-25			█													
IRI-1420	L2 - Plumbing In-Wal	10	0	0%	23-Jan-25	05-Feb-25			█													
Interior Fit Out		108	0	0%	30-Jan-25	01-Jul-25																
IRI-1400	L2 - Insulation / Drywall	30	0	0%	30-Jan-25	12-Mar-25			█													
IFO-1350	L2 - Painting / Walkcovering	20	0	0%	27-Feb-25	26-Mar-25				█												
IFO-1380	L2 - ACT Ceiling / Gyp Soffits	15	0	0%	13-Mar-25	02-Apr-25					█											
IFO-1370	L2 - MEP Trim Out	15	0	0%	20-Mar-25	09-Apr-25						█										
IFO-1320	L2 - Interior Glass / Glazing	5	0	0%	27-Mar-25	02-Apr-25						█										
IFO-1310	L2 - Finish Carpentry / Millwork	25	0	0%	01-Apr-25	05-May-25							█									
IFO-1340	L2 - Flooring	30	0	0%	22-Apr-25	03-Jun-25								█								
IFO-1390	L2 - Final Paint	15	0	0%	20-May-25	10-Jun-25									█							
IFO-1360	L2 - Furniture / Fixtures / Equipment	10	0	0%	04-Jun-25	17-Jun-25										█						
IFO-1410	L2 - Specialties (gym equip., lockers, etc.)	20	0	0%	04-Jun-25	01-Jul-25											█					
IFO-1330	L2 - Doors & Hardware	15	0	0%	11-Jun-25	01-Jul-25												█				
IFO-1400	L2 - Technology / AV Finishes	10	0	0%	11-Jun-25	24-Jun-25													█			
Level 1		135	0	0%	09-Jan-25	18-Jul-25																
Interior Rough In		53	0	0%	09-Jan-25	24-Mar-25																
IRI-1170	L1 - Plumbing OH	10	0	0%	09-Jan-25	22-Jan-25			█													
IRI-1160	L1 - Fire Protection	12	0	0%	27-Jan-25	11-Feb-25			█													
IRI-1180	L1 - HVAC / Controls	15	0	0%	03-Feb-25	21-Feb-25				█												
IRI-1150	L1 - Interior Studs	15	0	0%	10-Feb-25	28-Feb-25				█												
IRI-1190	L1 - Electrical	15	0	0%	24-Feb-25	14-Mar-25					█											
IRI-1200	L1 - Technology / AV	15	0	0%	24-Feb-25	14-Mar-25					█											
IRI-1310	L1 - Fire Alarm	10	0	0%	24-Feb-25	07-Mar-25					█											
IRI-1320	L1 - Plumbing In-Wal	10	0	0%	24-Feb-25	07-Mar-25					█											
IRI-1330	L1 - Door Frames / Storefronts	15	0	0%	04-Mar-25	24-Mar-25						█										
Interior Fit Out		93	0	0%	10-Mar-25	18-Jul-25																
IRI-1300	L1 - Insulation / Drywall	30	0	0%	10-Mar-25	18-Apr-25																
IFO-1160	L1 - Painting / Walkcovering	20	0	0%	07-Apr-25	02-May-25																
IFO-1270	L1 - ACT Ceiling / Gyp Soffits	15	0	0%	21-Apr-25	09-May-25																
IFO-1250	L1 - MEP Trim Out	15	0	0%	28-Apr-25	16-May-25																
IFO-1130	L1 - Interior Glass / Glazing	5	0	0%	05-May-25	09-May-25																

Start Date: 19-Dec-23
 Finish Date: 31-Oct-25
 Data Date: 31-Oct-24
 Run Date: 04-Nov-24 16:21
 Page 6 of 8
 SL-1

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Summary Milestones
- Critical Milestones
- Milestone

Shaker Ludlow

Activity ID	Activity Name	Original Duration	Actual Duration	Duration % Complete	Start	Finish	2025															
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec		
LND-1030	Waterproofing	20	0	0%	06-May-25	03-Jun-25																
LND-1000	Hardscapes	15	0	0%	04-Jun-25	24-Jun-25																
LND-1010	Landscaping	10	0	0%	25-Jun-25	09-Jul-25																
Long Lead Installation		90	0	0%	16-Apr-25	21-Aug-25																
LLI-1040	Transformer Installation	10	0	0%	16-Apr-25	29-Apr-25																
LLI-1030	Panelboards Installation	10	0	0%	30-Apr-25	13-May-25																
LLI-1050	Permanent Power	1	0	0%	14-May-25	14-May-25																
LLI-1020	Generator Installation	10	0	0%	08-Aug-25	21-Aug-25																
Closeout		86	0	0%	02-Jul-25	31-Oct-25																
CL-1050	Testing & Balancing	3	0	0%	02-Jul-25	07-Jul-25																
CL-1040	Commissioning	5	0	0%	08-Jul-25	14-Jul-25																
CL-1020	Final Clean	10	0	0%	21-Jul-25	01-Aug-25																
CL-1030	Final Inspections	1	0	0%	21-Jul-25	21-Jul-25																
CL-1060	Punchlist	74	0	0%	21-Jul-25	31-Oct-25																
CL-1000	First Day of School for Students	0	0	0%	27-Aug-25*																	
CL-1010	Closeout	15	0	0%	13-Oct-25	31-Oct-25																

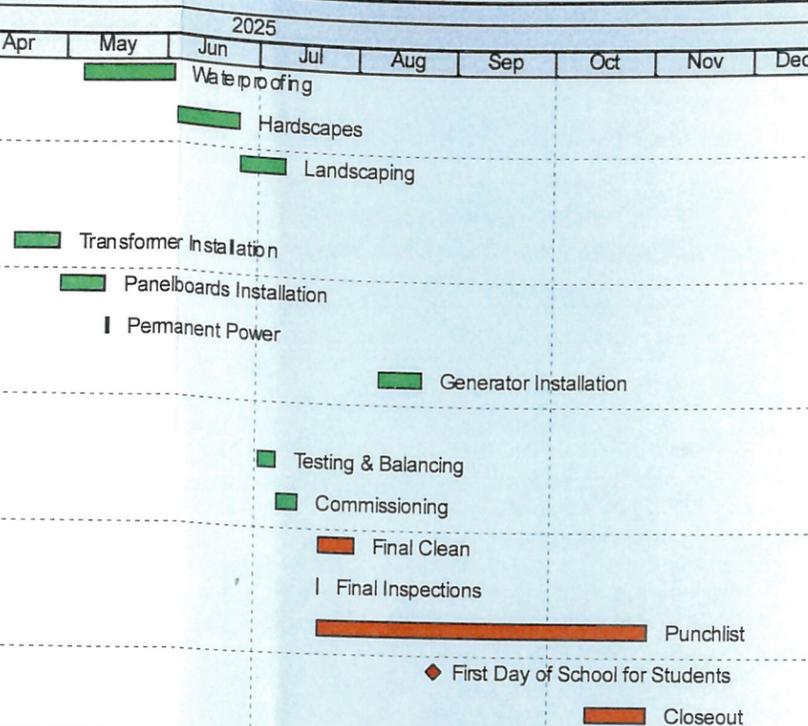

Start Date: 19-Dec-23
 Finish Date: 31-Oct-25
 Data Date: 31-Oct-24
 Run Date: 04-Nov-24 16:21
 Page 8 of 8
 SL-1

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Summary Milestones
- ◆ Critical Milestones
- ◆ Milestone

Shaker Ludlow
