

Activity ID	Activity Name	Original Duration	Start	Finish
Lomond Summary Schedule for review		669	27-Apr-26 A	06-Jul-29
Preconstruction		290	27-Apr-26 A	10-Jan-28
2027		290	27-Apr-26 A	10-Jan-28
Bid Package		141	27-Apr-26 A	13-Nov-26
A	SD	0	27-Apr-26 A	
A	DD-Issue for 2027 work	0	13-Nov-26	
A	IFC	0	13-Nov-26	
Budget/Appoval/Contract buy out		50	13-Nov-26	27-Jan-27
A	HVAC	50	13-Nov-26	27-Jan-27
A	Electrical	50	13-Nov-26	27-Jan-27
A	Roofing	50	13-Nov-26	27-Jan-27
A	Waterproofing	50	13-Nov-26	27-Jan-27
A	Mason	50	13-Nov-26	27-Jan-27
A	Concrete/site	50	13-Nov-26	27-Jan-27
A	Steel	50	13-Nov-26	27-Jan-27
A	Abatement Contractor	50	13-Nov-26	27-Jan-27
Shop drawing/ Submitals process		40	28-Jan-27	24-Mar-27
A	HVAC	40	28-Jan-27	24-Mar-27
A	Electrical	40	28-Jan-27	24-Mar-27
A	Roofing	30	28-Jan-27	10-Mar-27
A	Waterproofing	30	28-Jan-27	10-Mar-27
A	Mason	20	28-Jan-27	24-Feb-27
A	Concrete/site	20	28-Jan-27	24-Feb-27
A	Steel	40	28-Jan-27	24-Mar-27
Procurement		220	25-Feb-27	10-Jan-28
A	Mason	15	25-Feb-27	17-Mar-27
A	Concrete/site	15	25-Feb-27	17-Mar-27
A	Roofing	30	11-Mar-27	21-Apr-27
A	Waterproofing	25	11-Mar-27	14-Apr-27
A	HVAC/Curbs	40	25-Mar-27	19-May-27
A	Electrical/ Gear needed in 2028	200	25-Mar-27	10-Jan-28
A	Steel/ Roof	60	25-Mar-27	17-Jun-27
2028		0		
27' summer		39	07-Jun-27	30-Jul-27
A1300	Mob 27	5	07-Jun-27*	11-Jun-27
A1310	Exterior foundation Water Proofing (not timed repairs if required)	30	15-Jun-27	27-Jul-27
A1330	Basement abatement	20	15-Jun-27	13-Jul-27
A1320	New Flat Roof	30	18-Jun-27	30-Jul-27
A1690	Install Steel at roof	20	18-Jun-27	16-Jul-27
(New WBS)		0		
28 Main build		276	05-Jun-28	06-Jul-29
A1340	Owner Move out	0	05-Jun-28*	
A1350	Comise work	70	05-Jun-28	12-Sep-28
A1360	Abatement (inconclusive report)	30	06-Jun-28	18-Jul-28
A1370	Decommision/ Demo MEPS	15	06-Jun-28	26-Jun-28
A1380	First Energy De-engerize building	5	06-Jun-28	12-Jun-28

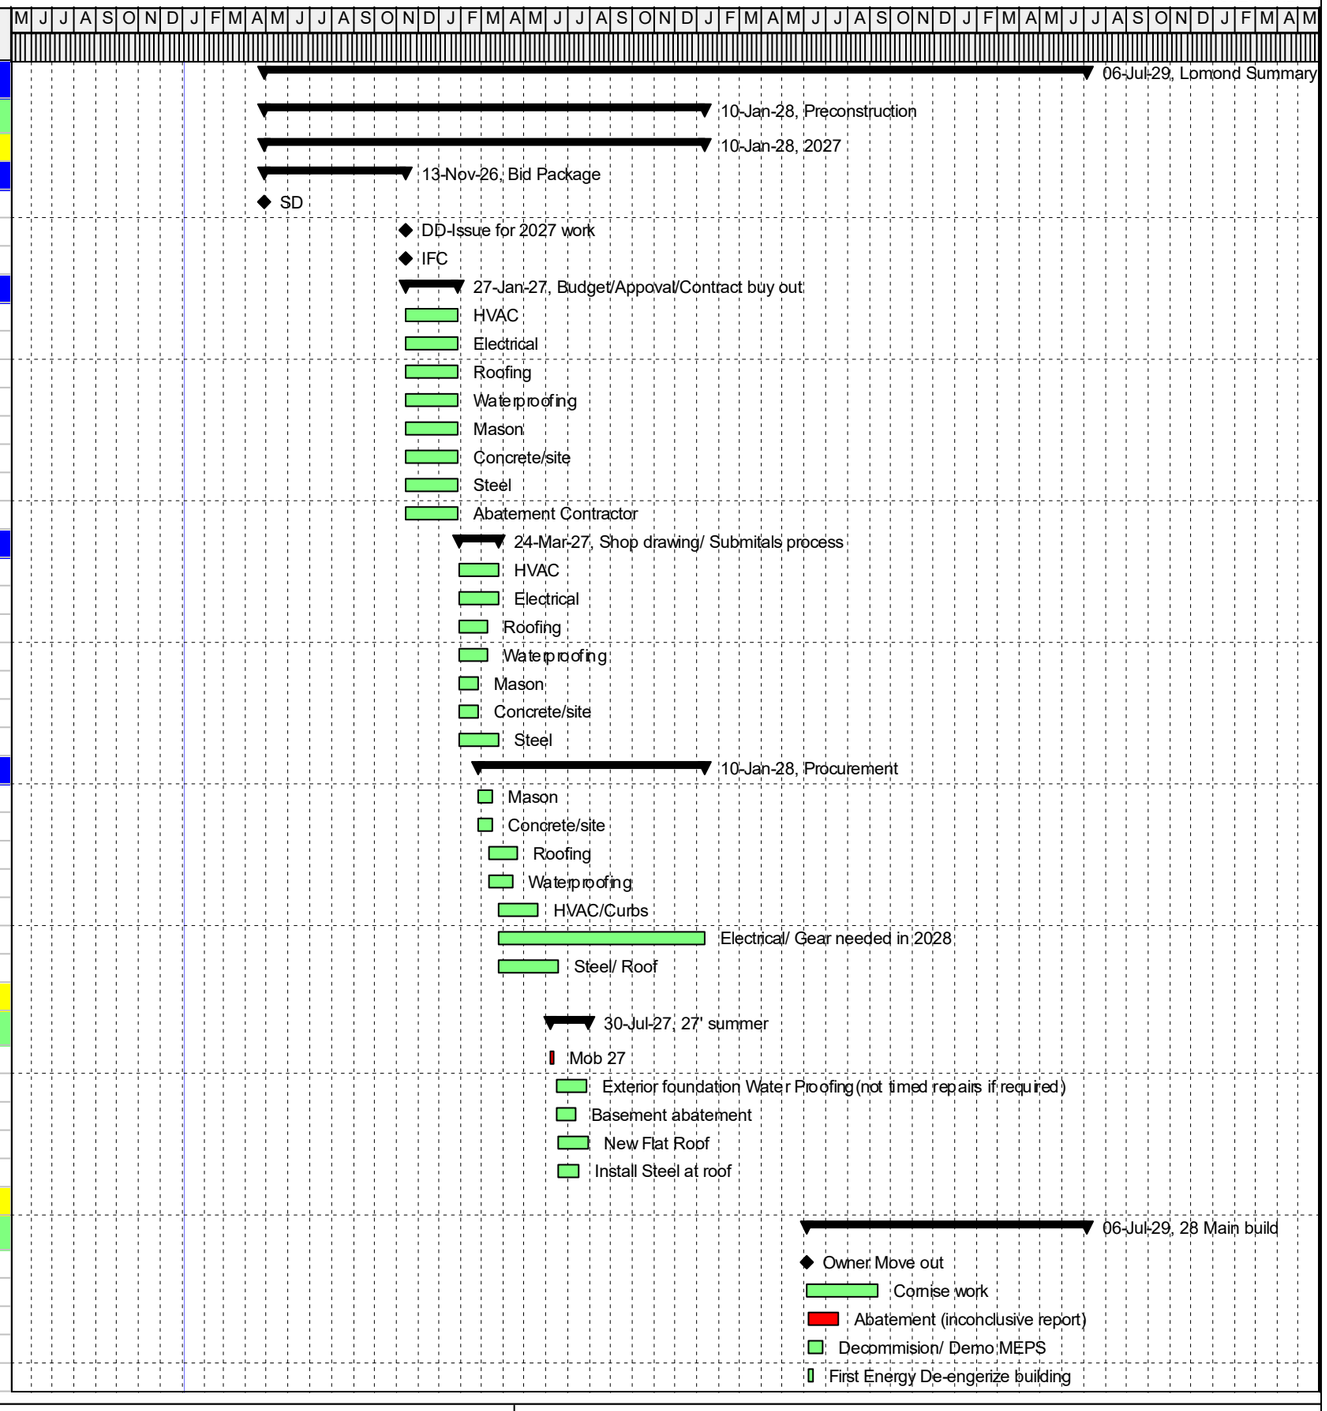

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Start	Finish
A1390	Reroute Main power (Lose Building power)	5	13-Jun-28	19-Jun-28
A1400	New Mechianical Yard	20	20-Jun-28	18-Jul-28
A1410	New Main Electrical Service	25	27-Jun-28	01-Aug-28
A1440	Interior Demo	40	19-Jul-28	13-Sep-28
A1420	Chiller install	10	19-Jul-28	01-Aug-28
A1430	Electrical distrbuition gear.	40	19-Jul-28	13-Sep-28
A1450	New Electrical Service go live	0	02-Aug-28	
A1460	Interior structual demo/install	30	09-Aug-28	20-Sep-28
A1470	Interior rough build out	100	16-Aug-28	10-Jan-29
A1480	AHUs (8)	40	23-Aug-28	18-Oct-28
A1490	Demo/Install Slat roof (based on existing sub-straight in good conditions)	80	13-Sep-28	09-Jan-29
A1500	Slab infills	30	21-Sep-28	01-Nov-28
A1510	New foundation work/ elevator	10	21-Sep-28	04-Oct-28
A1520	Elevator install	20	05-Oct-28	01-Nov-28
A1530	HVAC goes live	0	09-Nov-28	
A1540	Finishes	100	09-Nov-28	04-Apr-29
A1550	Civil/Pavement parking	30	10-Jan-29	20-Feb-29
A1560	Site work	20	21-Feb-29	20-Mar-29
A1570	Punchlist activities	45	05-Apr-29	07-Jun-29
A1580	Owner move-in	20	08-Jun-29	06-Jul-29
A1590	First day of school	0		06-Jul-29

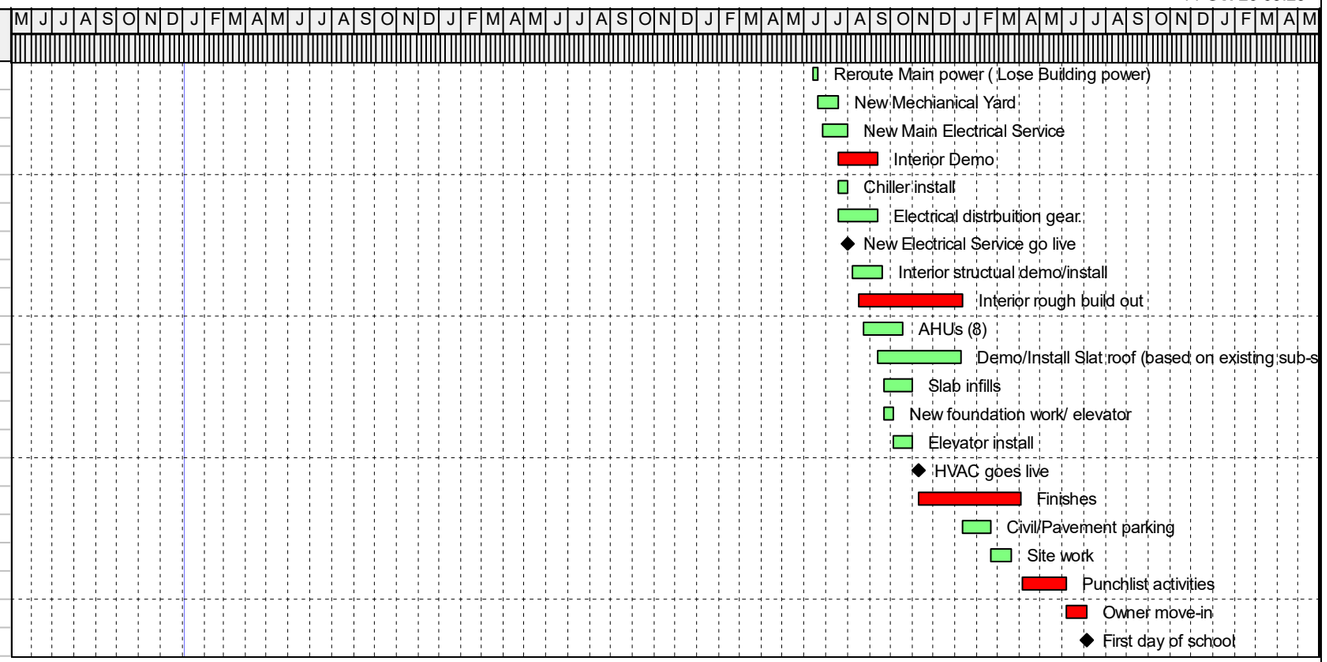

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

© Oracle Corporation
