
Activity ID	Activity Name	Original Duration	Start	Finish
Mercer Summary Schedule		824	27-Apr-26	27-Jul-29
Preconstruction		420	27-Apr-26	23-Dec-27
2027		420	27-Apr-26	23-Dec-27
Bid Package		125	27-Apr-26	22-Oct-26
A	SD	0	27-Apr-26	
A	DD	0	15-Oct-26	
A	IFC	0	22-Oct-26	
Budget/Appoval/Contact buy out		50	15-Oct-26	29-Dec-26
A	Roofing	50	15-Oct-26	29-Dec-26
A	Electrical	50	15-Oct-26	29-Dec-26
A	HVAC	50	15-Oct-26	29-Dec-26
A	Waterproofing	50	15-Oct-26	29-Dec-26
A	Concrete/site work	50	15-Oct-26	29-Dec-26
Shop drawing/ Submitals		50	30-Dec-26	10-Mar-27
A	Roofing	50	30-Dec-26	10-Mar-27
A	Electrical	50	30-Dec-26	10-Mar-27
A	HVAC	50	30-Dec-26	10-Mar-27
A	Waterproofing	50	30-Dec-26	10-Mar-27
A	Concrete/site work	50	30-Dec-26	10-Mar-27
Procurment		200	11-Mar-27	23-Dec-27
A	Roofing	30	11-Mar-27	21-Apr-27
A	Electrical	200	11-Mar-27	23-Dec-27
A	HVAC	200	11-Mar-27	23-Dec-27
A	Waterproofing	25	11-Mar-27	14-Apr-27
A	Concrete/site work	15	11-Mar-27	31-Mar-27
2028		0		
Budget/Appoval/Contract Buy out		0		
Shop Drwaing/Submitlas		0		
Procurment		0		
2027 summer		35	07-Jun-27	26-Jul-27
A1740	MOB 27	5	07-Jun-27*	11-Jun-27
A1750	Exterior Foundation Water proofing (not timed for repairs if required)	30	14-Jun-27	26-Jul-27
A1760	Equipment abatement	20	14-Jun-27	12-Jul-27
A1770	New Roofing (based on mainting exisiting drain locations)	30	14-Jun-27	26-Jul-27
2028 Main build		291	05-Jun-28	27-Jul-29
A1290	Owner Move out/Mob	5	05-Jun-28*	09-Jun-28
A1350	Decommision/ Demo MEPS	15	12-Jun-28	30-Jun-28
A1300	Abatement (inconclusive report)	30	13-Jun-28	25-Jul-28
A1310	Exterior foundation Water Proofing/ Drainage	30	13-Jun-28	25-Jul-28
A1320	First Energy De-engerize building	5	13-Jun-28	19-Jun-28
A1330	New Main Power/ Water (Lose Building power)	20	20-Jun-28	18-Jul-28
A1370	Interior Demo	40	05-Jul-28	29-Aug-28
A1450	New Flat Roof	30	12-Jul-28	22-Aug-28
A1780	Roof steel	15	12-Jul-28	01-Aug-28
A1340	New Mechianical Yard structures	30	19-Jul-28	29-Aug-28
A1410	Interior rough build out	100	26-Jul-28	18-Dec-28



Actual Work · Critical Remaining Work · Summary
Remaining Work · Milestone

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Start	Finish
A1360	Comise work	70	26-Jul-28	01-Nov-28
A1400	Interior structual demo	15	26-Jul-28	15-Aug-28
A1420	New foundations	10	16-Aug-28	29-Aug-28
A1460	AHUs (6)	40	23-Aug-28	18-Oct-28
A1380	New Main Electrical Service	25	30-Aug-28	04-Oct-28
A1390	Chiller install	10	30-Aug-28	13-Sep-28
A1430	Structual Reenforcing for AHUs	20	30-Aug-28	27-Sep-28
A1440	Electrical distrbuition gear.	40	07-Sep-28	01-Nov-28
A1470	New Electrical Service go live	0	02-Nov-28	
A1490	HVAC goes live	0	02-Nov-28	
A1480	Elevator modifications	10	02-Nov-28	16-Nov-28
A1500	Finishes	100	05-Dec-28	25-Apr-29
A1510	Civil/Pavement parking	30	05-Dec-28	17-Jan-29
A1520	Site work	25	22-Mar-29	25-Apr-29
A1530	Punchlist activities	45	26-Apr-29	28-Jun-29
A1540	Owner move-in	20	29-Jun-29	27-Jul-29
A1550	First day of school	0		27-Jul-29

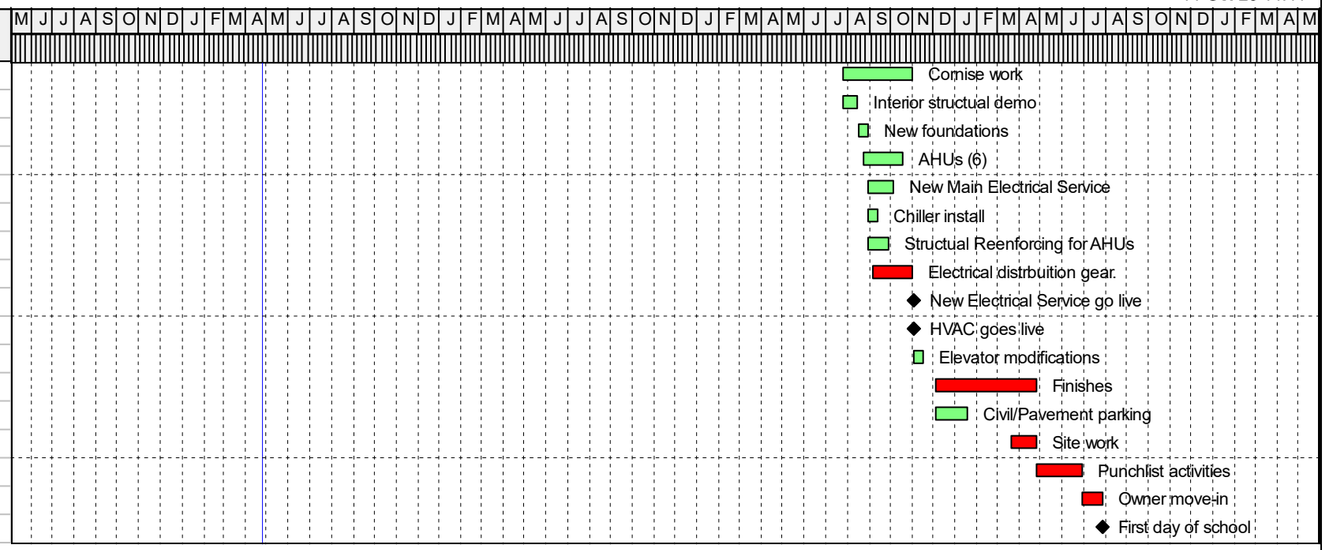

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

© Oracle Corporation
